








ID	Task Name	Duration	Start	Finish	February			
					1/27	2/3	2/10	2/17
1	Preconstruction Meeting	1d	1/28/08	1/28/08				
2	Notice To Proceed	0d	3/19/08	3/19/08				
3	Submittals	11d	3/19/08	4/2/08				
4	Mobilization	6d	3/19/08	3/26/08				
5	Traffic Control & Regulation - Pha. I & II	99d	3/19/08	8/4/08				
6	Tree and Plant Protection - Pha. I, II & III	10d	3/19/08	4/1/08				
7	TPDES Requirements - Pha. I & II	99d	3/19/08	8/4/08				
8	Flagmen - Pha. I & II	99d	3/19/08	8/4/08				
9	Phase I - Step 1	68d	3/19/08	6/20/08				
10	Construct Detour on East Side of Bunker Hill - IH 10 to Bridge	11d	3/19/08	4/2/08				
11	Construct 12" Water Line	54d	3/19/08	6/2/08				
12	Construct 6" Sanitary Force Main & 8" Sanitary Sewer	30d	5/12/08	6/20/08				
13	Phase I - Step 2	44d	4/1/08	5/30/08				
14	Construct W. Side of Bunker Hill Incl. Rd. Removal, Excav., Stabilization & Paving	44d	4/1/08	5/30/08				
15	Phase I, II & III	87d	5/1/08	8/29/08				
16	Construct Traffic Signal at Village Plaza	87d	5/1/08	8/29/08				
17	Phase I & II	56d	5/15/08	7/31/08				
18	Install Street Light Conduit & Construct Concrete Driveways & Sidewalks	56d	5/15/08	7/31/08				
19	Install Softscape Related Items	34d	6/16/08	7/31/08				
20	Phase II	44d	6/2/08	7/31/08				
21	Construct E. Side of Bunker Hill Incl. Rd. Removal, Excav., Stabilization & Paving	44d	6/2/08	7/31/08				
22	Phase III	21d	8/1/08	8/29/08				








Project: Bunker Hill Road
Date: 3/19/08

Task  Summary  Rolled Up Progress 








Progress  Rolled Up Task 

Milestone  Rolled Up Milestone 

ID	Task Name	Duration	Start	Finish	February			
					1/27	2/3	2/10	2/17
23	Traffic Control & Regulation	21d	8/1/08	8/29/08				
24	TPDES Requirements	21d	8/1/08	8/29/08				
25	Flagmen	21d	8/1/08	8/29/08				
26	Construction of Bridge at W 140-01-00	21d	8/1/08	8/29/08				
27	Phase IV	45d	9/1/08	10/31/08				
28	Traffic Control & Regulation	45d	9/1/08	10/31/08				
29	Tree and Plant Protection	45d	9/1/08	10/31/08				
30	TPDES Requirements	45d	9/1/08	10/31/08				
31	Flagmen	45d	9/1/08	10/31/08				
32	Phase IV - Step 1	9d	9/2/08	9/12/08				
33	Construct Temp. Asph. Paving on E. Side of Bunker Hill - Bridge to Cedardale & W. Side of Bunker Hill	9d	9/2/08	9/12/08				
34	Phase IV - Step 2	20d	9/15/08	10/10/08				
35	Construct W. Side of Bunker Hill- Bridge to Pine Lake & S. Side of Pine Lake Incl. Rd. Removal, Str	20d	9/15/08	10/10/08				
36	Phase IV - Steps 3 & 4	34d	9/16/08	10/31/08				
37	Construct N. Side of Pine Lake and W. Side of Bunker Hill - Pine Lake to Cedardale	14d	9/16/08	10/3/08				
38	Construct E. Side of Bunker Hill - Cedardale to Long Point Road	21d	10/3/08	10/31/08				
39	Phase IV & V	66d	10/1/08	12/31/08				
40	Install Street Light Conduit & Construct Concrete Driveways & Sidewalks	63d	10/6/08	12/31/08				
41	Construct Traffic Signal at Bunker Hill & Westview	66d	10/1/08	12/31/08				
42	Install Softscape Related Items	30d	11/17/08	12/26/08				
43	Phase V	43d	11/3/08	12/31/08				
44	Traffic Control & Regulation	43d	11/3/08	12/31/08				

Project: Bunker Hill Road Date: 3/14/08	Task		Summary		Rolled Up Progress	
	Progress		Rolled Up Task			
	Milestone		Rolled Up Milestone			




ID	Task Name	Duration	Start	Finish	February			
					1/27	2/3	2/10	2/17
45	Tree and Plant Protection	43d	11/3/08	12/31/08				
46	TPDES Requirements	43d	11/3/08	12/31/08				
47	Flagmen	43d	11/3/08	12/31/08				
48	Phase V - Steps 1 & 2	43d	11/3/08	12/31/08				
49	Construct E. Side of Bunker Hill - Bridge to Cedardale	20d	11/3/08	11/28/08				
50	Construct W. Side of Bunker Hill - Cedardale to Long Point, Incl. Rd. Removal, Str. Swr., Excav., S	23d	12/1/08	12/31/08				
51	Phase VI - VIII	41d	1/2/09	2/27/09				
52	Traffic Control & Regulation	41d	1/2/09	2/27/09				
53	Tree and Plant Protection	41d	1/2/09	2/27/09				
54	TPDES Requirements	41d	1/2/09	2/27/09				
55	Flagmen	41d	1/2/09	2/27/09				
56	Phase VI - Steps 1 & 2	16d	1/2/09	1/23/09				
57	Construct Temporary Asphalt Lane on N. Side of Westview	4d	1/2/09	1/7/09				
58	Construct S. Side of Westview Incl. Rd. Removal, Str. Swr., Excav., Stabilization & Paving	13d	1/7/09	1/23/09				
59	Phase VII	14d	1/26/09	2/12/09				
60	Construct Middle Lane of Westview Incl. Rd. Removal, Excavation, Stabilization & Paving	14d	1/26/09	2/12/09				
61	Phase VIII	32d	1/15/09	2/27/09				
62	Construct N. Side of Westview Incl. Rd. Removal, Excavation, Stabilization & Paving	11d	2/13/09	2/27/09				
63	Construct Concrete Driveways & Sidewalks	32d	1/15/09	2/27/09				
64	Phase IX & X	65d	3/2/09	5/29/09				
65	Traffic Control & Regulation	65d	3/2/09	5/29/09				
66	Tree and Plant Protection	65d	3/2/09	5/29/09				


Project: Bunker Hill Road Date: 3/14/08	Task		Summary		Rolled Up Progress	
	Progress		Rolled Up Task			
	Milestone		Rolled Up Milestone			


ID	Task Name	Duration	Start	Finish	February			
					1/27	2/3	2/10	2/17
67	TPDES Requirements	65d	3/2/09	5/29/09				
68	Flagmen	65d	3/2/09	5/29/09				
69	Construct Traffic Signal at Bunker Hill & Long Point	14d	3/4/09	3/23/09				
70	Construct Concrete Driveways & Sidewalks	55d	3/16/09	5/29/09				
71	Phase IX - Steps 1 & 2	33d	3/4/09	4/17/09				
72	Construct Temporary Asphalt on N. & S. Sides of Long Point	6d	3/4/09	3/11/09				
73	Construct S. Side of Long Point Incl. Rd. Removal, Str. Swr., Excav., Stabilization and Paving	27d	3/12/09	4/17/09				
74	Phase X	30d	4/20/09	5/29/09				
75	Construct N. Side of Long Point Incl. Rd. Removal, Excav., Stabilization & Paving	30d	4/20/09	5/29/09				
76	Project Clean Up and Demobilization	18d	5/18/09	6/10/09				
77	Project Complete - Begin Closeout Procedures	0d	6/11/09	6/11/09				

Project: Bunker Hill Road
Date: 3/19/08





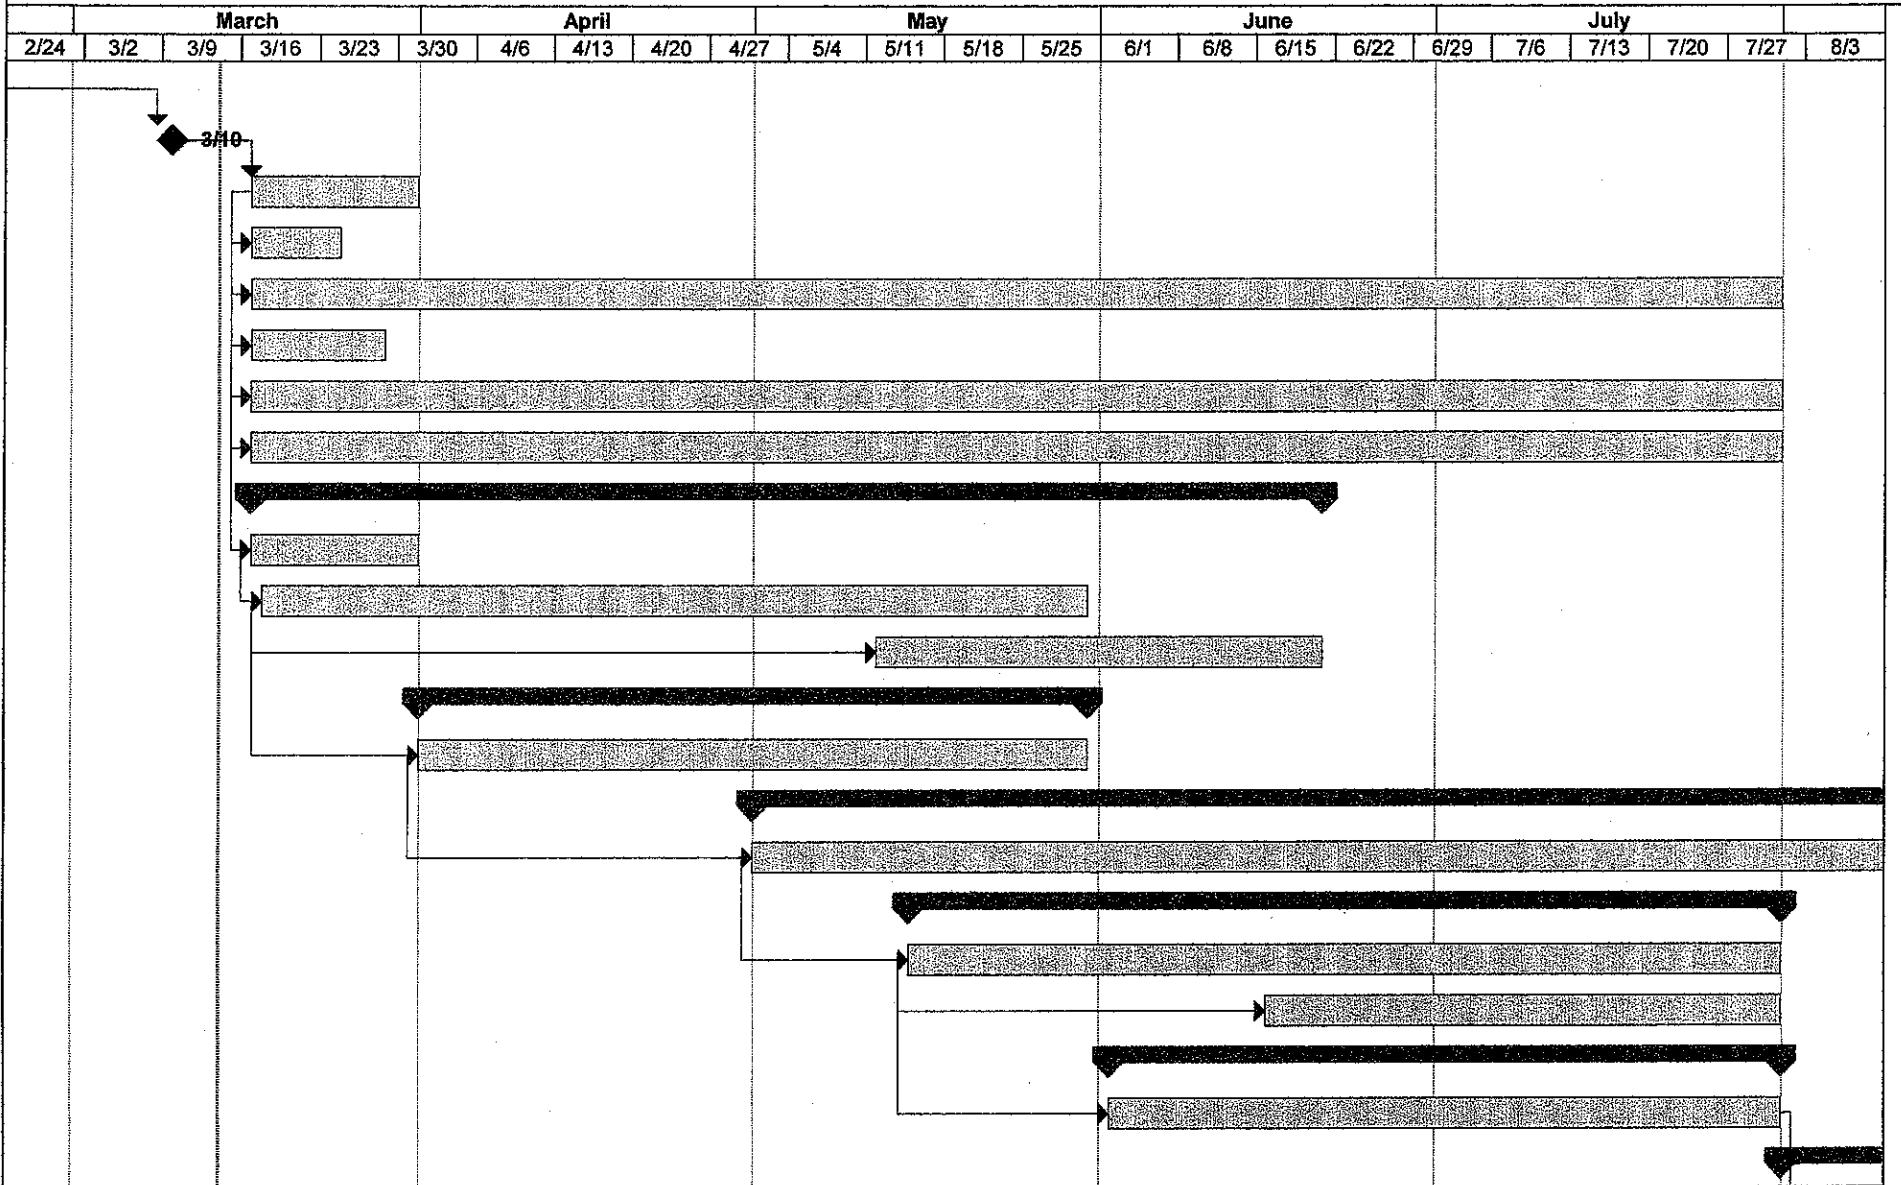


Task 
 Progress 
 Milestone 

Summary 
 Rolled Up Task 
 Rolled Up Milestone 


Rolled Up Progress 



Project: Bunker Hill Road
Date: 3/14/08




Task		Summary		Rolled Up Progress	
Progress		Rolled Up Task			
Milestone		Rolled Up Milestone			

March			April				May				June				July									
2/24	3/2	3/9	3/16	3/23	3/30	4/6	4/13	4/20	4/27	5/4	5/11	5/18	5/25	6/1	6/8	6/15	6/22	6/29	7/6	7/13	7/20	7/27	8/3	



Project: Bunker Hill Road
Date: 3/14/08

Task 
 Progress 
 Milestone 

Summary 
 Rolled Up Task 
 Rolled Up Milestone 


Rolled Up Progress 

March			April				May				June				July									
2/24	3/2	3/9	3/16	3/23	3/30	4/6	4/13	4/20	4/27	5/4	5/11	5/18	5/25	6/1	6/8	6/15	6/22	6/29	7/6	7/13	7/20	7/27	8/3	


Project: Bunker Hill Road
Date: 3/14/08

Task 

Progress 

Milestone 

Summary 

Rolled Up Task 




Rolled Up Milestone 

Rolled Up Progress 

March			April				May				June				July									
2/24	3/2	3/9	3/16	3/23	3/30	4/6	4/13	4/20	4/27	5/4	5/11	5/18	5/25	6/1	6/8	6/15	6/22	6/29	7/6	7/13	7/20	7/27	8/3	

Project: Bunker Hill Road
Date: 3/14/08

Task 
 Progress 
 Milestone 


Summary 
 Rolled Up Task 
 Rolled Up Milestone 

Rolled Up Progress 





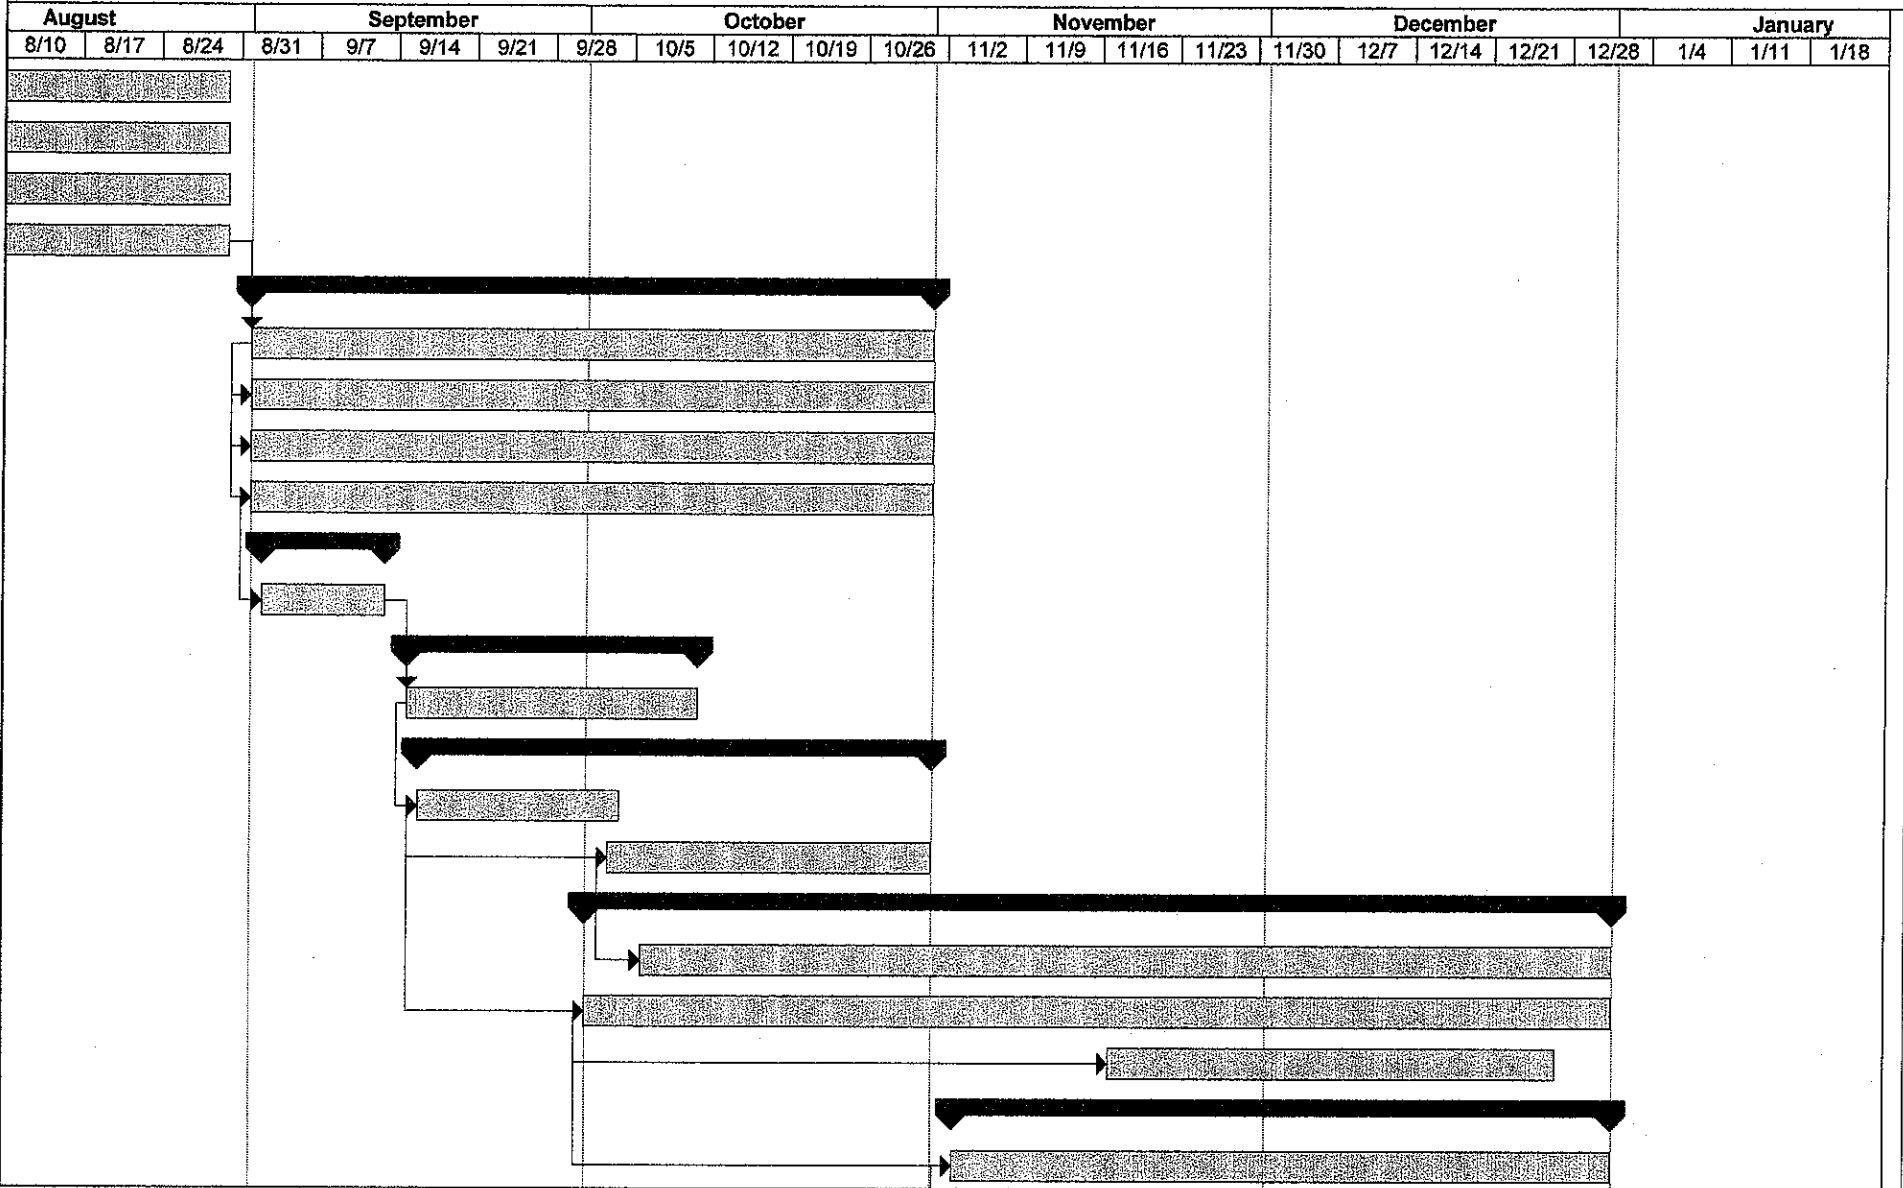


August			September				October				November				December				January				
8/10	8/17	8/24	8/31	9/7	9/14	9/21	9/28	10/5	10/12	10/19	10/26	11/2	11/9	11/16	11/23	11/30	12/7	12/14	12/21	12/28	1/4	1/11	1/18
[Task Bar]																							
[Task Bar]																							
[Task Bar]																							


Project: Bunker Hill Road
Date: 3/14/08

- Task 
- Progress 
- Milestone 
- Summary 
- Rolled Up Task 
- Rolled Up Milestone 
- Rolled Up Progress 




Project: Bunker Hill Road
Date: 3/14/08

Task		Summary		Rolled Up Progress	
Progress		Rolled Up Task			
Milestone		Rolled Up Milestone			

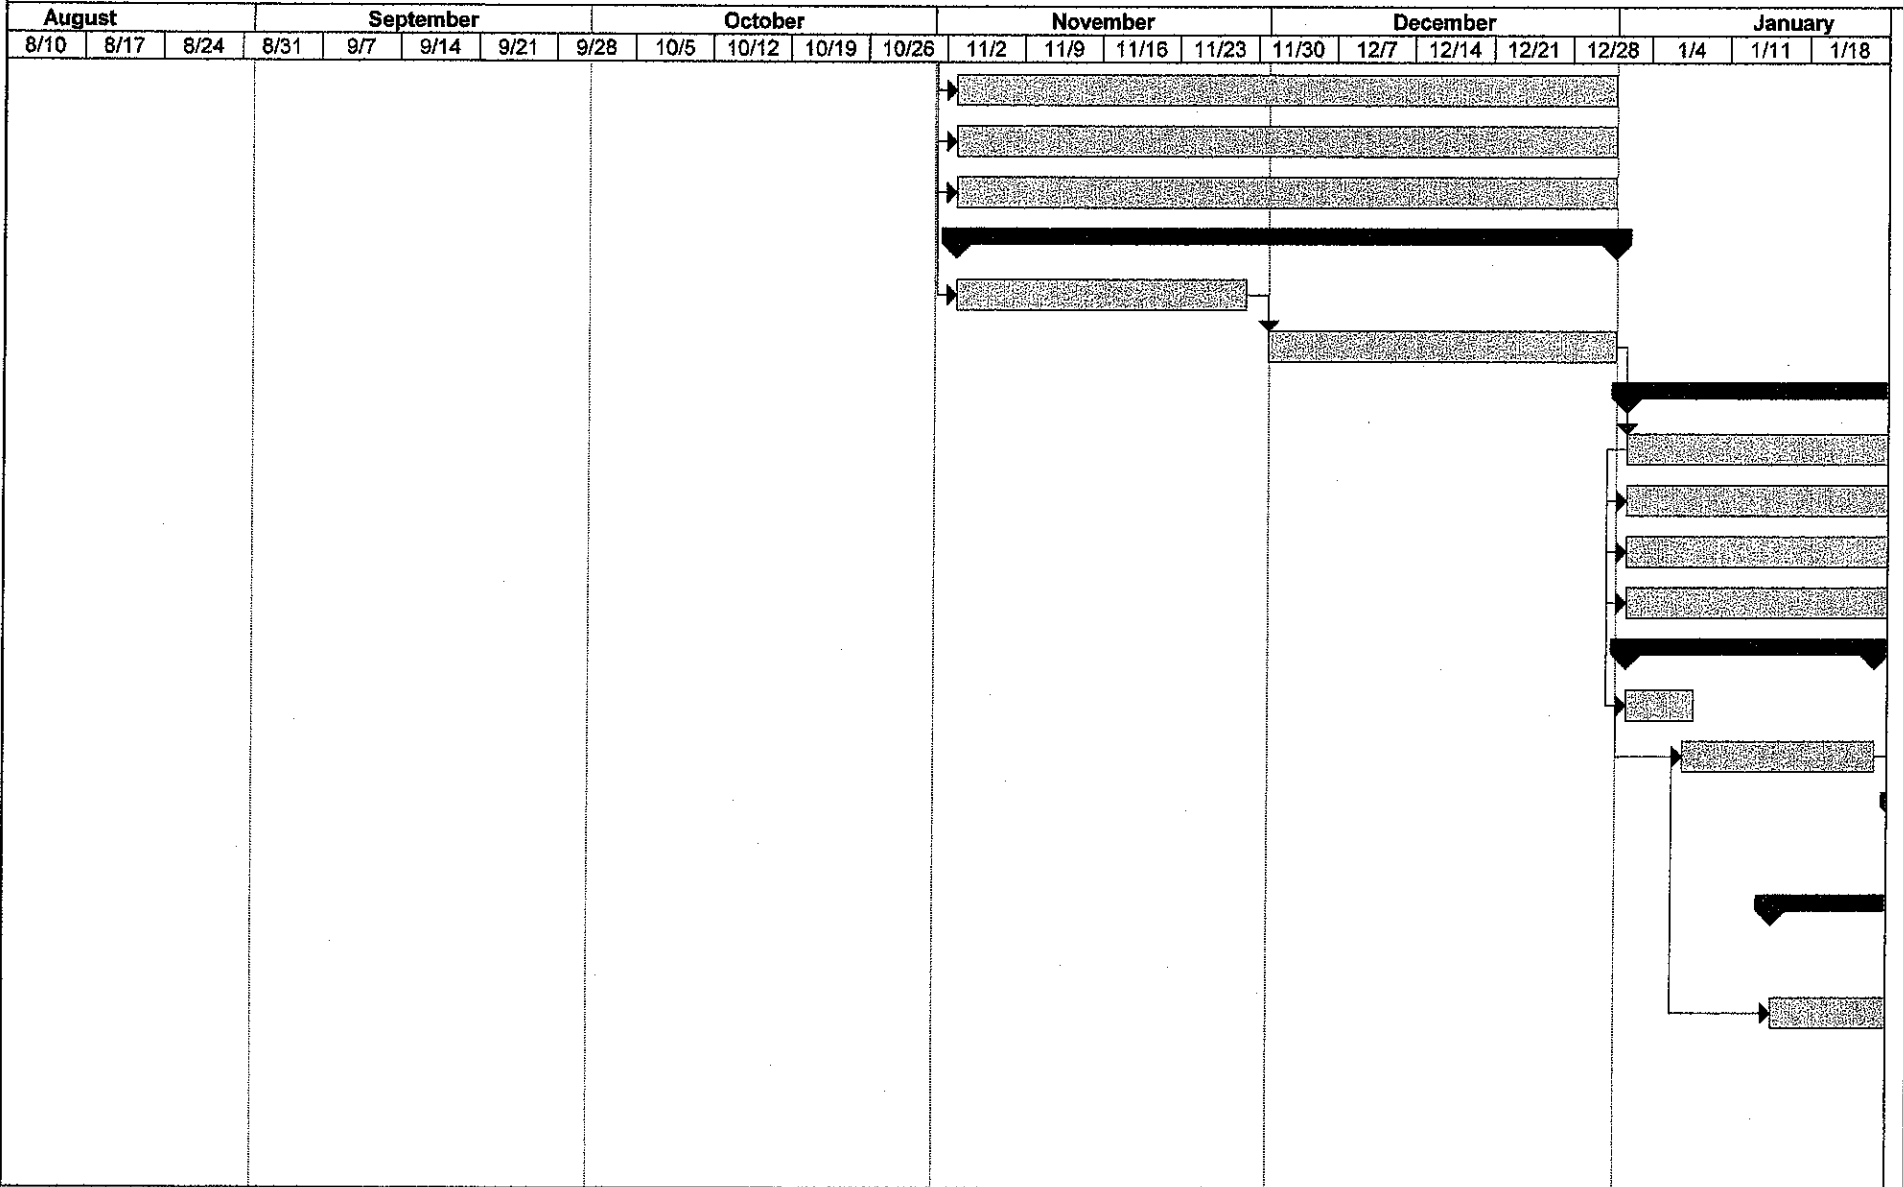

Project: Bunker Hill Road
Date: 3/14/08

Task 
 Progress 
 Milestone 




Summary 
 Rolled Up Task 
 Rolled Up Milestone 

Rolled Up Progress 

August			September				October				November				December				January				
8/10	8/17	8/24	8/31	9/7	9/14	9/21	9/28	10/5	10/12	10/19	10/26	11/2	11/9	11/16	11/23	11/30	12/7	12/14	12/21	12/28	1/4	1/11	1/18

Project: Bunker Hill Road
Date: 3/14/08








Task 
 Progress 
 Milestone 

Summary 
 Rolled Up Task 
 Rolled Up Milestone 








Rolled Up Progress 


	February				March				April				May				June						
1/25	2/1	2/8	2/15	2/22	3/1	3/8	3/15	3/22	3/29	4/5	4/12	4/19	4/26	5/3	5/10	5/17	5/24	5/31	6/7	6/14	6/21	6/28	7/5

Project: Bunker Hill Road
Date: 3/14/08


Task		Summary		Rolled Up Progress	
Progress		Rolled Up Task			
Milestone		Rolled Up Milestone			

	February				March				April				May				June						
1/25	2/1	2/8	2/15	2/22	3/1	3/8	3/15	3/22	3/29	4/5	4/12	4/19	4/26	5/3	5/10	5/17	5/24	5/31	6/7	6/14	6/21	6/28	7/5

Project: Bunker Hill Road Date: 3/14/08	Task 	Summary 	Rolled Up Progress 
	Progress 	Rolled Up Task 	
	Milestone 	Rolled Up Milestone 	

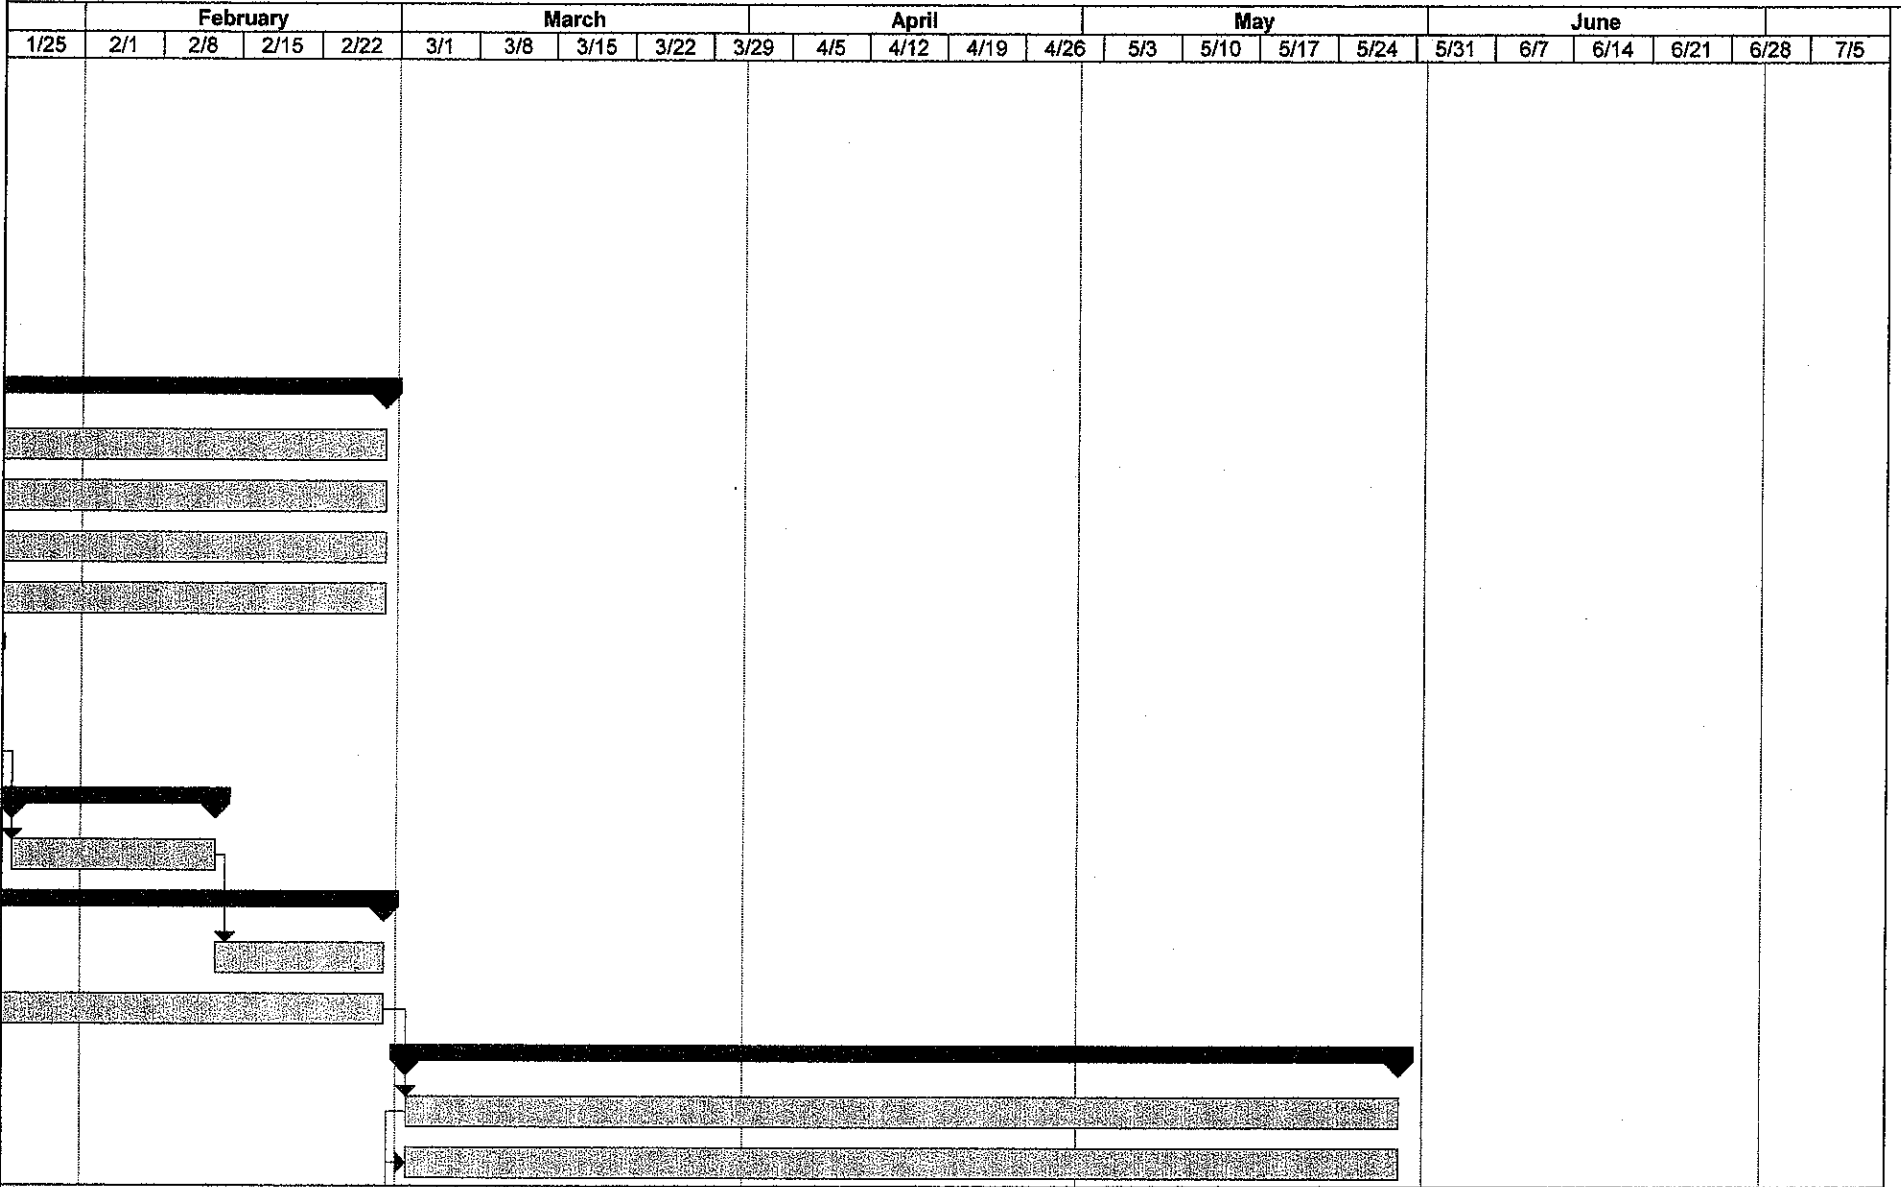

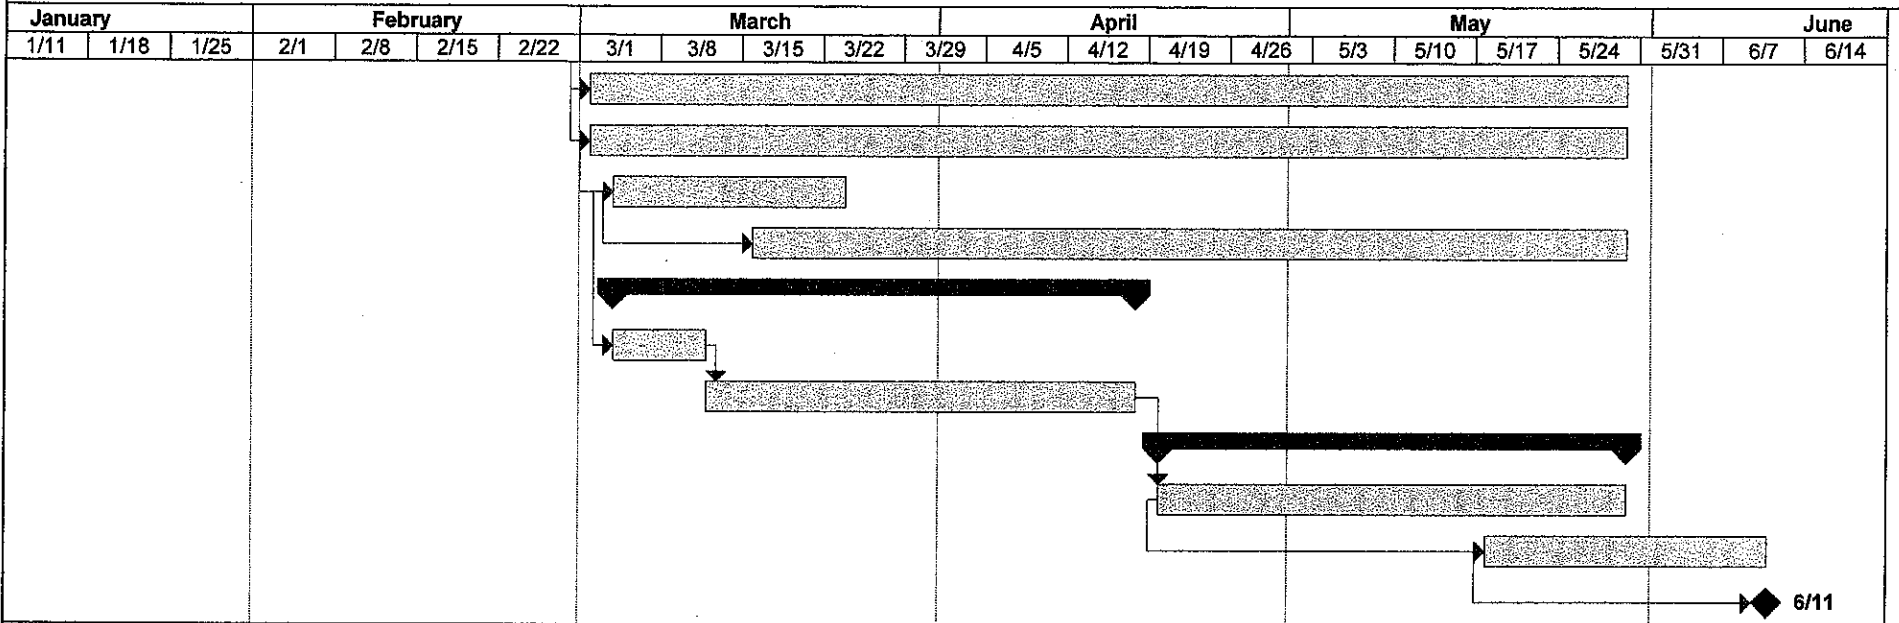


Project: Bunker Hill Road Date: 3/14/08	Task		Summary		Rolled Up Progress	
	Progress		Rolled Up Task			
	Milestone		Rolled Up Milestone			



Project: Bunker Hill Road
Date: 3/19/08

Task 
Progress 
Milestone 

Summary 
Rolled Up Task 
Rolled Up Milestone 

Rolled Up Progress 
