

Lumpkin Road

Reconstruction and Drainage Improvements
WBS No. N-T17000-0012-3

TIRZ 17


REDEVELOPMENT

AUTHORITY



Project Location

The project is located along Lumpkin Road between IH10 Frontage Road and Northbrook Drive. City Council District A.

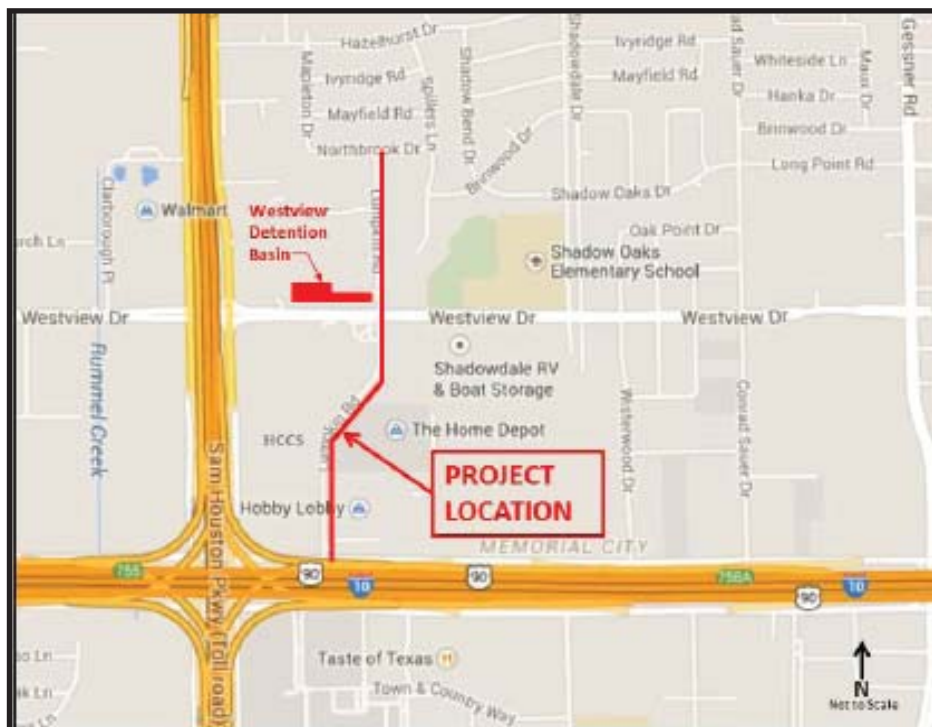

Not to scale

Project Purpose

The purpose of the Project is to improve vehicular and pedestrian flow, improve local and regional drainage with the installation reinforced concrete box storm sewers and with improvements to the existing detention basin at the northwest corner of Lumpkin Road and Westview Drive, which will result in increased conveyance and storage.

Project Description

The overall construction will consist of installation of storm sewer facilities ranging in size from 4'x4' to dual 8'x8' boxes, detention basin improvements, replacement of water and sanitary sewer lines, relocation of large diameter water transmission lines, installation of three (3) lanes of concrete pavement, and sidewalks throughout the project limits. Also included will be a bus shelter, pedestrian lights along the western sidewalks, pavers and trees. The traffic signal at Westview Drive will also be upgraded to meet current City of Houston Standards.

Status Report

- Completed driveways and sidewalks along Lumpkin Rd. , north of Westview Dr.
- Completed detention basin
- Completed storm drain connection between Spillers Ln. and Lumpkin Rd.
- Started substantial completion inspections and documentation.

Current Traffic Control Configuration

- All streets have two-way traffic

Construction Schedule

Construction Phases	Schedule Completion
Phase 1 - West side from I-10 frontage road to Westview Drive -Install water line along west side -Install storm boxes -Construct concrete paving and sidewalks along west side.	July 2015
Phase 2 - East side from I-10 frontage road to Westview Drive -Construct concrete paving, sidewalks and lighting	October 2015
Phase 3 - Lumpkin Road and Westview Dr. Intersection -Relocate 36" and 48" water lines -Install storm boxes through intersection -Construct concrete paving	April 2015
Phase 4 - Lumpkin Road at Westview Dr. -Install storm sewer at detention basin -Construct detention basin -Install sanitary sewer	September 2015
Phase 5 - Lumpkin Road between Westview Dr. and Northbrook Dr. -Install storm sewer system -Install water lines -Construct concrete paving, sidewalks and lighting	January 2016

Payment Estimates	
Original contract amount	\$11,142,521.40
Change order amount to date	\$3,083,429.26
Current contract amount	\$14,225,950.66
Previous payments	\$13,169,505.23
Current payment due (Est. Nos. 13 & 14)	\$718,731.27
Contract completion date	April 14, 2016

* For more information please refer to TIRZ 17 website



Basin after March 9 -10, 2016 rain event



Basin after March 9 -10, 2016 rain event



48-inch storm drain installation to Spillers Ln. cul-de-sac

Construction Time:

- Contract time is 465 calendar days.
- Notice to Proceed date – January 5, 2015

Contact Information:

Construction Manager (CM):
Lockwood, Andrews, and Newnam, Inc. (LAN)
2925 Briarpark Dr., Suite 400
Houston, TX 77042

Contractor:
SER Construction Partners, LLC
3636 Pasadena Blvd.
Pasadena, TX 77503
