

Status Report: December 2018/January 2019

Town & Country West Drainage & Mobility Improvements (T-1717)

Reconstruction and Drainage Improvements
WBS No. N-T17000-0014-7

TIRZ 17

REDEVELOPMENT

AUTHORITY

Project Location

A portion of this project is located along Town & Country Way between Beltway 8 frontage road and Town & Country Lane, south of IH-10. The other portion of this project is located along Town & Country Boulevard between Town & Country Way and IH-10 Frontage Road. This project is located in City Council District G.



Status Report

- Completing Punchlist
- Preparing Close-Out Documents

Project Purpose

Improve drainage by increasing conveyance and storage

- Oversized reinforced concrete storm sewer box culverts will provide approximately 6.5 acre-feet of storage

Improve mobility, safety, and quality of life

- Extending Town & Country Way west to the Beltway 8 Northbound Frontage Road
- Installing a roundabout at the new intersection of Town & Country Way and Town & Country Boulevard
- Adding pedestrian friendly wider sidewalks, gathering area, and various other softscape/hardscape elements
- Replacing aging public utilities that have exceeded their useful service life

Project Description

The overall construction will consist of installation of oversized subsurface storm water detention system using reinforced concrete storm sewer boxes ranging in size from 6'x9' to 10'x10'; re-aligning Town & Country Blvd and Town & Country Way to eliminate the existing 75' street offset, construction of a one-lane roundabout at the new intersection of Town & Country Blvd and Town & Country Way, and construction of a new 3-lane concrete roadway extending Town & Country Way west to Beltway 8 frontage road, and replacement of water and sanitary sewer lines. The project will also include enhanced concrete sidewalks, paved crosswalks, pedestrian lighting, street lighting, enhanced landscaping and special paved areas for public gathering.

Status Report: December 2018/January 2019

Town & Country West Drainage & Mobility Improvements (T-1717)

Construction Schedule

Construction Phase	Scheduled Completion
Phase 1: Public Utilities <ul style="list-style-type: none">Install all proposed waterlinesInstall all proposed sanitary sewer lines	Nov. 2017
Phase 2: Town & Country Blvd <ul style="list-style-type: none">Install storm sewer boxesReconstruct Town & Country Blvd	April 2018
Phase 3: Town & Country Way <ul style="list-style-type: none">Install storm sewer boxesConstruct new extension road to Beltway 8Construct western half of roundabout	May 2018
Phase 4: Roundabout <ul style="list-style-type: none">Install storm sewer boxesConstruct eastern half of roundaboutReconstruct Town & Country Way east to Town & Country Lane	Sep. 2018

Payment Estimates

Original Contract Amount	\$8,478,677.80
Change Order Amount to Date	\$49,865.00
Current Contract Amount	\$8,528,542.80
Previous Payments	\$6,439,474.62
Current Payment Due (Est. No. 15)	\$336, 337.12
Contract Completion Date (Time Extension in Review)	9/13/2018

Construction Time

- Contract time is 365 calendar days.
- Notice to Proceed date: September 12, 2017

Contact Information

Construction Manager (CM)

Lockwood, Andrews, and Newnam, Inc. (LAN)
2925 Briarpark Dr., Suite 400
Houston, TX 77042

Contractor


SER Construction Partners, LLC
3636 Pasadena Blvd.
Pasadena, TX 77503

For more information please visit www.houstontirz17.org

Progress Photos



Plaza looking north

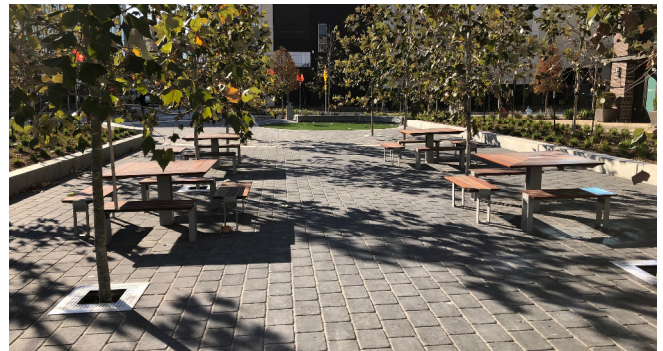

Plaza looking south



Town & Country Way looking west



Town & Country Blvd. looking north
