


PROGRESS REPORT—AUGUST 2019

Briar Branch (W140-01-00) Channel & Straws Improvements

WBS No. N-T17000-0018-3, T-1734 & T-1734B

PROJECT LOCATION

The channel improvement project is approximately 6,200 feet long, from Gessner Road east to Oak Tree Drive, approximately 1,750 feet east of Bunker Hill Road. This project is located in City Council District A.

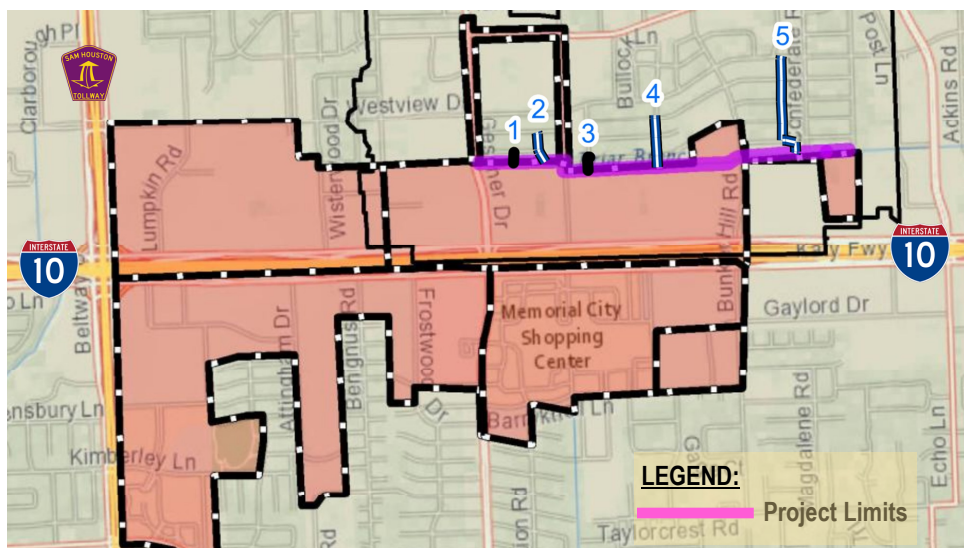

PROJECT STATUS

- Storm box sewers are currently being installed west of Bunker Hill Rd.
- Worked with City and Contractor to resolve 3 wastewater line conflicts.
- Work on straw no. 5 (Spring Rock Lane) continues to progress (90% complete), pavement work done.
- Retaining wall work scheduled for completion early September.

CURRENT TRAFFIC CONTROL CONFIGURATION

- All streets are open
- Northbound Bunker Hill Road is shifted towards the east at Bunker Hill crossing

PROJECT OBJECTIVE

Improve drainage by increasing conveyance and storage

The Briar Branch (W140-01-00) Channel & Straws Improvements project involves the construction of storm drainage improvements that are designed to lower water levels on Briar Branch, provide flood mitigation storage, and deliver flooding relief and protection to the surrounding community.

PROJECT DESCRIPTION

- The channel improvement project is approximately 6,200 feet long, from Gessner Road east to Oak Tree Drive, approximately 1,750 feet east of Bunker Hill Road. The proposed channel improvements will include constructing box culverts ranging in size from 7-FT x 7-FT to 10-FT x 8-FT RCBs along the length of the system, effectively enclosing the channel.
- The Straw improvements consist of approximately 2,600 linear feet of perpendicular improvements at five (5) separate lateral locations along Briar Branch, from Gessner Road east to Confederate Lane, approximately 1,000 feet east of Bunker Hill Road.
- Included in the channel improvements is the reconstruction of the Bunker Hill Road crossing at Briar Branch from dual 7-FT x 7-FT RCBs to triple 8'x8' RCBs.

Cont. PROGRESS REPORT—AUGUST 2019

Briar Branch (W140-01-00) Channel & Straws Improvements

WBS No. N-T17000-0018-3, T-1734 & T-1734B

CONSTRUCTION TIME

- Contract time: 24 Months
- Notice to Proceed date: December 17, 2018

CONTACT INFORMATION

Construction Manager (CM)

Gauge Engineering
3200 Wilcrest Drive, Suite 220
Houston, TX 77042



Contractor

Reytec Construction Resources
1901 Hollister St.
Houston, TX 77080



PAYMENT ESTIMATES

Original Contract Amount	\$18,794,957.00
Change Order Amount to Date	\$0.00
Current Contract Amount	\$18,794,957.00
Previous Payments	\$7,363,375.08
Current Payment Due	\$1,962,159.16
Contract Completion Date	11/30/2020
Balance Remaining	\$8,978,605.17

PROGRESS PHOTOS



RCB installation west of Bunker Hill Road — Phase II



Pouring floor in junction box near Gessner Road



Repaving of Springrock Lane



Repaving of Bunker Hill Road
