


PROGRESS REPORT—MAY 2021

Briar Branch (W140-01-00) Channel & Straws Improvements

WBS No. N-T17000-0018-3, T-1734 & T-1734B

PROJECT LOCATION

The channel improvement project is approximately 6,200 feet long, from Gessner Road east to Oak Tree Drive, approximately 1,750 feet east of Bunker Hill Road. This project is located in City Council District A.

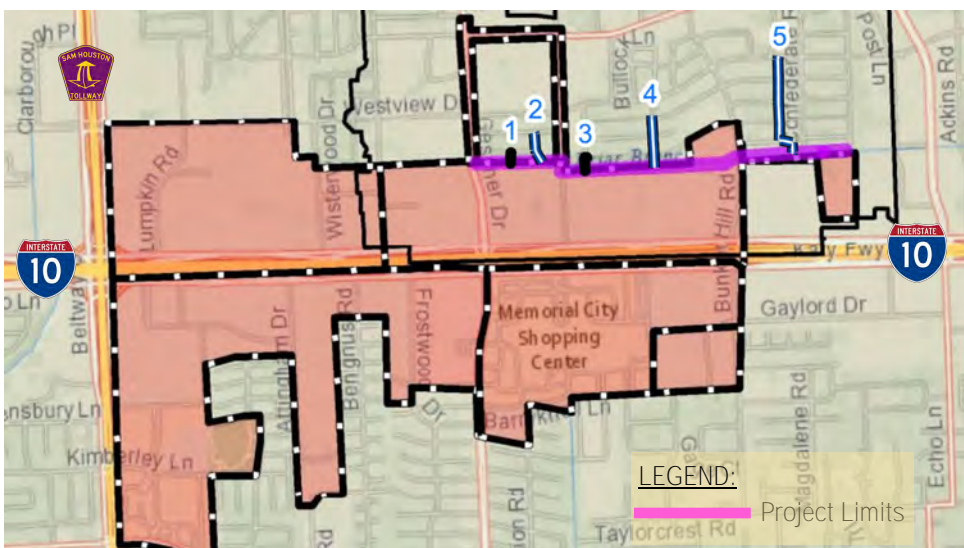

PROJECT STATUS

- Finished addressing punch list items from substantial completion walkthrough
- Installed mid-block crossing at Bunker Hill Rd

CURRENT TRAFFIC CONTROL CONFIGURATION

- All roads are fully open

PROJECT OBJECTIVE

Improve drainage by increasing conveyance and storage

The Briar Branch (W140-01-00) Channel and Straws Improvements project involves the construction of storm drainage improvements that address and reduce the risk of structural flooding in this area.

PROJECT DESCRIPTION

- The channel improvement project is approximately 6,200 feet long, from Gessner Road east to Oak Tree Drive, approximately 1,750 feet east of Bunker Hill Road. The proposed channel improvements will include constructing box culverts ranging in size from 7-FT x 7-FT to 10-FT x 8-FT RCBs along the length of the system, effectively enclosing the channel.
- The Straw improvements consist of approximately 2,600 linear feet of perpendicular improvements at five separate lateral locations along Briar Branch, from Gessner Road east to Confederate Lane, approximately 1,000 feet east of Bunker Hill Road.
- Included in the channel improvements is the reconstruction of the Bunker Hill Road crossing at Briar Branch from dual 7-FT x 7-FT RCBs to triple 8'x8' RCBs.

Cont. PROGRESS REPORT—MAY 2021

Briar Branch (W140-01-00) Channel & Straws Improvements

WBS No. N-T17000-0018-3, T-1734 & T-1734B

CONSTRUCTION TIME

- Original Contract time: 24 Months
- Notice to Proceed date: December 17, 2018

CONTACT INFORMATION

Construction Manager (CM)
Gauge Engineering
3200 Wilcrest Drive, Suite 220
Houston, TX 77042



Contractor
Reytec Construction Resources
1901 Hollister St.
Houston, TX 77080



PAYMENT ESTIMATES

| | |
|-----------------------------|---|
| Original Contract Amount | \$18,794,957.00 |
| Change Order Amount to Date | \$259,449.13 |
| Current Contract Amount | \$19,054,406.13 |
| Previous Payments | \$18,081,264.64 |
| Current Payment (s) Due | \$218,897.64 |
| Contract Completion Date | Original 12/21/2020 Extended: 6/1/2021 |
| Balance Remaining | \$873,190.84 |

PROGRESS PHOTOS



Crosswalk Island Completion - Bunker Hill Rd



Concrete Pour for sidewalk - Bunker Hill Rd



Truncated Domes Installation - Bunker Hill Rd



Ramp Work Completed—Bunker Hill Rd
