

PROGRESS REPORT— MAY 2026

BRIAR BRANCH STORM WATER DETENTION BASIN EXPANSION AND STORM SEWER IMPROVEMENTS

WBS No. N-T7000-0021-3



PROJECT LOCATION

Storm sewer and roadway improvements:

Westview Drive, Cedardale Dr, Windhover Ln, and Demaret Ln

Basin improvements:

At existing basin between Bunker Hill Rd and Blalock Rd.

FUNDING PARTNERS

EPA: \$3,394,000

PROJECT OBJECTIVES & DESCRIPTION

Reduce risk of flooding in neighborhood by:

- Installing reinforced concrete boxes to draw water more quickly away from the homes.
- Mitigating flow increases by deepening the detention basin.

ASSOCIATED IMPROVEMENTS

- Reinforced concrete boxes and basin deepening
- Half-road replacement
- Mill and overlay roadway (side without boxes)
- Sidewalk and ADA-compliant wheelchair ramps
- Waterline replacements
- Driveway replacement
- Lift station
- Subsurface barrier wall

EXISTING BASIN



Existing Roadway



PROJECT STATUS

- Completed storm sewer installation in neighborhood.
- Completed other half roadway pavement.
- Completed pilot channel.
- Basin excavation is complete.
- Installation of wet well components continued.
- Waiting on Building Permit

NEXT STEPS

- Continue lift station internal components.
- Continue basin access road
- Continue lift station and channel lining/weir work after building permit.

BASIN DETENTION VOLUME

Pre-project volume: 44 ac-ft
Added volume: 35.1 ac-ft*
Total: 79.2 ac-ft

*80% capacity increase

PROGRESS REPORT— MAY 2026

BRIAR BRANCH STORM WATER DETENTION BASIN EXPANSION AND STORM SEWER IMPROVEMENTS



CONSTRUCTION TIME

Original Contract Time: 470 Days
Mobilization Date: Jan 6th, 2025

CONTACT INFORMATION

Construction Manager:
HR Green
11750 Katy Freeway, Suite 400
Houston, TX 77079



CONTRACTOR

Reytec Construction Resources, Inc.
1901 Hollister St.
Houston, TX 77080



PAYMENT ESTIMATES

Original Contract Amount	\$13,797,688.00
Change Order Amount to Date	\$0.00
Current Contract Amount	\$13,797,688.00
Previous Payments	\$11,017,271.75
Current Payment Due (Minus Retainage)	\$292,399.13
Contract Completion Date	April 20, 2026
Balance Remaining	\$2,388,018.21


PROGRESS PHOTOS



Vegetative Growth in Basin



Sod Strips in Basin

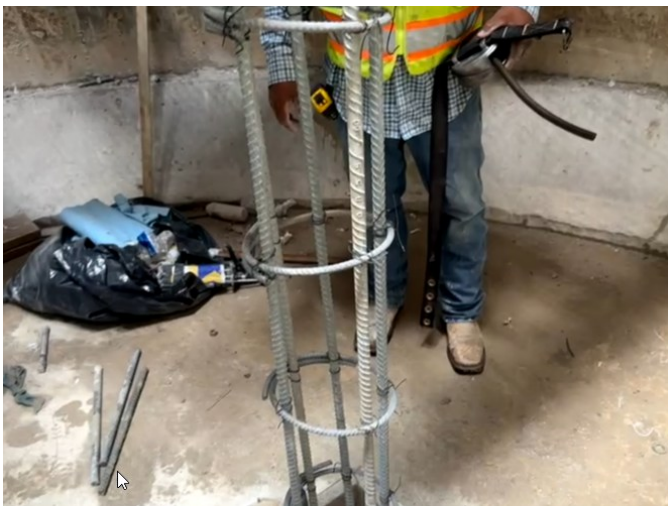

Rebar for Column



Basin with Rainwater
