Status Report: November 2018


Town & Country West Drainage & Mobility Improvements (T-1717)

Reconstruction and Drainage Improvements WBS No. N-T17000-0014-7



Project Location

A portion of this project is located along Town & Country Way between Beltway 8 frontage road and Town & Country Lane, south of IH-10. The other portion of this project is located along Town & Country Boulevard between Town & Country Way and IH-10 Frontage Road. This project is located in City Council District G.

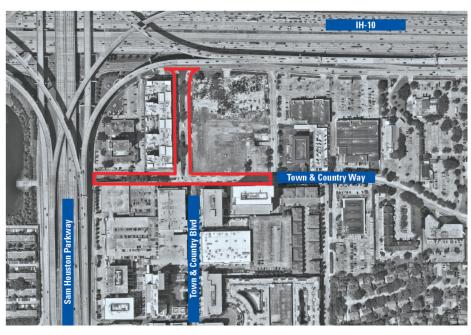

Status Report

- Completed plaza
- Completed landscaping
- Completed signage and pavement markings
- SER requested Substantial Completion

Project Purpose

Improve drainage by increasing conveyance and storage

Oversized reinforced concrete storm sewer box culverts will provide approximately 6.5 acre-feet of storage

Improve mobility, safety, and quality of life

- Extending Town & Country Way west to the Beltway 8 Northbound Frontage Road
- Installing a roundabout at the new intersection of Town & Country Way and Town & Country Boulevard
- Adding pedestrian friendly wider sidewalks, gathering area, and various other softscape/hardscape elements
- · Replacing aging public utilities that have exceeded their useful service life

Project Description

The overall construction will consist of installation of oversized subsurface storm water detention system using reinforced concrete storm sewer boxes ranging in size from 6'x9' to 10'x10'; re-aligning Town & Country Blvd and Town & Country Way to eliminate the existing 75' street offset, construction of a one-lane roundabout at the new intersection of Town & Country Blvd and Town & Country Way, and construction of a new 3-lane concrete roadway extending Town & Country Way west to Beltway 8 frontage road, and replacement of water and sanitary sewer lines. The project will also include enhanced concrete sidewalks, pavered crosswalks, pedestrian lighting, street lighting, enhanced landscaping and special pavered areas for public gathering.

Town & Country West Drainage & Mobility Improvements (T-1717)

Construction Schedule

Construction Phase	Scheduled Completion
 Phase 1: Public Utilities Install all proposed waterlines Install all proposed sanitary sewer lines 	Nov. 2017
 Phase 2: Town & Country Blvd Install storm sewer boxes Reconstruct Town & Country Blvd 	April 2018
 Phase 3: Town & Country Way Install storm sewer boxes Construct new extension road to Beltway 8 Construct western half of roundabout 	May 2018

Phase 4: Roundabout

- Install storm sewer boxes
- Construct eastern half of roundabout Sep. 2018
- Reconstruct Town & Country Way east to Town & Country Lane

Payment Estimates

_	
Original Contract Amount	\$8,478,677.80
Change Order Amount to Date	\$49,865.00
Current Contract Amount	\$8,528,542.80
Previous Payments	\$6,439,474.62
Current Payment Due (Est. No. 14)	\$406,379.46
Contract Completion Date (Time Extension Requested)	9/13/2018

Construction Time

- Contract time is 365 calendar days.
- Notice to Proceed date: September 12, 2017

Contact Information

Construction Manager (CM)

Lockwood, Andrews, and Newnam, Inc. (LAN) 2925 Briarpark Dr., Suite 400 Houston, TX 77042

Contractor

SER Construction Partners, LLC 3636 Pasadena Blvd. Pasadena, TX 77503

For more information please visit www.houstontirz17.org

Progress Photos



Plaza looking north



Plaza looking south



Town & Country Way looking west



Town & Country Blvd. looking north
